Proposal for the development of Web based IT Hardware Asset Management System for LSGD Principal Directorate, Kerala.

TECHNICAL & FINANCIAL PROPOSAL

Prepared By

IPROMISE SOLUTIONS

REF: IPROM/PRP/18.v2
Date: 16-July-2025
Trivandrum, Kerala

IPROMISE SOLUTIONS

Table of Contents

1 COMPANY PROFILE – IPROMISE SOLUTIONS 2

2 ABOUT OF THE PROJECT 2

3 SCOPE OF WORK FOR IPROMISE TEAM 3

4 DEVELOPMENT– APPROACH & METHODOLOGY 3

4.1 Our Approach towards implementing system features 3

4.2 Our Development Methodology 4

5 PROPOSED TECHNOLOGIES & PLATFORMS 4

6 PROJECT SCOPE - FEATURES OR MODULES 4

7 IMPLEMENTATION PLAN 7

8 PROJECT ORGANIZATION STRUCTURE 8

9 PROJECT ESTIMATION 8

10. RESPONSIBILITIES 10

11 PROJECT RELATED ASSUMPTIONS 10

12 TIME LINE 10

12 SUPPORT - SLA 11

13 CONTACT US 12

1 COMPANY PROFILE – IPROMISE SOLUTIONS

IPROMISE SOLUTIONS PVT LTD is a strategic business unit formed with the objective of providing pro-active advantage to its clients through on-demand quality services at competitive prices. IPROMISE is operating in Trivandrum-India, as an independent software development and IT/e-Governance Support service provider, our corporate office located at 2nd floor, Penta city Tower, Killipalam ,Trivandrum and our software development center located at Ramanathapuram , Coimbatore. It is led by a highly qualified Management & Technical team with experience in Web development and e-Governance support services domains. With core focus on Web & Mobile Application Development, IT Support & Social Media marketing services, it always strives to provide the best industry solutions to its clients.

IPROMISE is a togetherness of smarter people with high passion and dedication to dig the way to the ultimate solution. What IPROMISE provides to the clients, is unmatched for, be it in quality of work or helping to maximize client's business. The business processes we follow are unique which ensures highly optimized products delivered at the right time with high quality.

2 ABOUT OF THE PROJECT

This proposal outlines the development and implementation of a comprehensive web-based IT Hardware asset management System for the LSGD Directorate, Government of Kerala. The system aims to streamline the process of providing educational resources to students, ensuring efficient management and access control, and facilitating real-time monitoring and reporting.

The primary objectives of the proposed Hardware asset management System are as follows:

- Enable Super admin to create institution accounts.
- Provide admin login credentials to institutions for enrollment.
- Allow institutional users to Host and manage details of IT assets belongs to their institutions. (Computers, Laptops, Printers, Photocopiers, Softwares, Antivirus, Network Switches, Smartphones etc..)

- Allow Superadmin to categorize and subcategorize IT Hardwares.
- Capture detailed metadata (Title, Make, Model, Sl.No., Spec,Warranty, AMC etc.) for each Asset.
- Facilitate real-time monitoring and reporting on user activity.
- Allocation of IT assets to Officers / Sections.
- Alerts to office Admins regarding the Expiry of warranty/ AMC.
- Service History logs
- Report Generation (Office Wise, AMC wise, Warranty Wise, Category wise etc.)

3 SCOPE OF WORK FOR IPROMISE TEAM

IPROMISE shall carry out this project in accordance with the accepted Requirement Specification and deliverables for developing the mobile application. For developing the Application IPROMISE defines the following scope:

- Development of UI/UX for the Application
- Customizations of Features
- Unit testing and Integration testing
- Support for production management

4 DEVELOPMENT– APPROACH & METHODOLOGY

4.1 Our Approach towards implementing system features



Figure: Implementation Approach

4.2 Our Development Methodology

Figure: Development Methodology

5 PROPOSED TECHNOLOGIES & PLATFORMS

1. Web Admin Panel & Web Customer Portal
    a. **PHP CodeIgniter & MySQL** (Customize according to the module needs)

6 PROJECT SCOPE - FEATURES OR MODULES

Sl No	Project Process
1	SRS Documentation & Prototypes
2	Design Phase
3	Development
4	Unit & Regression Testing
5	User Acceptance Testing (UAT)
6	Final Deployment, Training
7	LIVE

Modules:

The Hardware Asset Management System will offer the following features:

1. **Account Management**

   - **Super Admin Privileges:**
     - Can create and manage accounts for each institution/ suboffice/ Sections .

   - **Institutional Admin Access**:
     - Each institution will be assigned an admin account called Office Admins.
     - Office Admins are responsible for enrolling officers and managing their assets (IT hardware Assets).

2. **Officer Enrollment and Verification**

   - **Enrollment Process:**
     - Institutional Admins enroll officers.
     - Verification belongs to that office admins responsibility.
     - Only verified officers can access the system.

3. **Access Control**

   - **Role-based Permissions:**
     - Officers and users are restricted to access and manage IT asset data pertaining only to their own office.
     - Inter-office data visibility is given to superior officers as per the office hierarchy.

4. **Hardware Asset Management**

   - **Asset Entry:**
     - Office Admins add IT hardware assets belonging to their institution.

   - **Mandatory Metadata Fields:**
     - Asset Title, Make, Model, Serial Number, Specification, Warranty Details, AMC Details, etc.

   - **Asset Allocation:**
     - Office Admins can allocate assets to officers or internal sections .

Private & Confidential – Ipromise Solutions Pvt. Ltd.

5. **Reports Generation**

- **Custom and Standard Reports- Generate Reports Based on Multiple Parameters:**
  - Consolidated Reports – For Super Admin (department-wise and office-wise).
  - Purchase Date/ Period wise Reports – (department-wise and office-wise).
  - AMC-wise Reports – (department-wise and office-wise).
  - Warranty-wise Reports – (department-wise and office-wise).
  - Category-wise Reports – (department-wise and office-wise).
  - Service History Reports – (department-wise and office-wise).

- **Service History:**
  - Maintain and export service and maintenance records for each asset. This should be updated by the office Admins in time.

6. **Dashboard & Analytics:**
   - Summary statistics of assets will be displayed on the Super Admin dashboard department-wise, and office-wise statistics will be shown on the Office Admins' dashboard

7. **Notifications**
   - **Email-Based Notifications:**
     - Used for account verification and alerts.
     - Officer verification includes validating PEN Number and official email address.

   - **Optional SMS Alerts:**
     - SMS gateway integration can be enabled for login & password details sharing.(optional – additional charges may apply for the SMS gateway).

Private & Confidential – Ipromise Solutions Pvt. Ltd.

7 IMPLEMENTATION PLAN

Phases	Modules	Process Detail
Phase 1	SRS Documentation (Detailed discussion with client on the options & fields) Designs& Prototype Project Planning, Architecture Designing & Environment setups	In this phase detailed system document will be shared along with the designs for approval. Document includes the work flows, functionalities, field level details etc.
Phase 2	Development: • Web Admin Panel • User web Portal	Base core modules will be delivered at this phase. Also identify the gaps if any based on the user experience or validation at the time of submission of each module
Phase 3	UAT Phase 2	Client shall test along with our Analyst team to check all the requirements has been completed in the test server and if any issues shall work over this period for the completion of Phase 2
Release Delivery		

Delivery Terms:

- Onsite review / clarification turnaround time shall be within three to four working days from the date of the receipt of the deliverables.
- Any major change will have an impact on the deliverable and this may have a cascading effect on the other deliverables depending on its complexity.
- The 15 days maintenance support (for beta testing) is a value add to the customer and is valid from UAT sign off date
- The training provided on System is targeted to train the trainers.
- Requires a lead time of 7-15 business days for the Project Kick off from the date of proposal and contract sign off

Deliverables:

1. Software Requirement Specification Document (SRS Doc)
2. Wireframes & Prototypes
3. Functional Requirements Document
4. Web User Interface
5. Web Admin Panel
6. Application source Code (Web)

Private & Confidential – Ipromise Solutions Pvt. Ltd.

8 PROJECT ORGANIZATION STRUCTURE

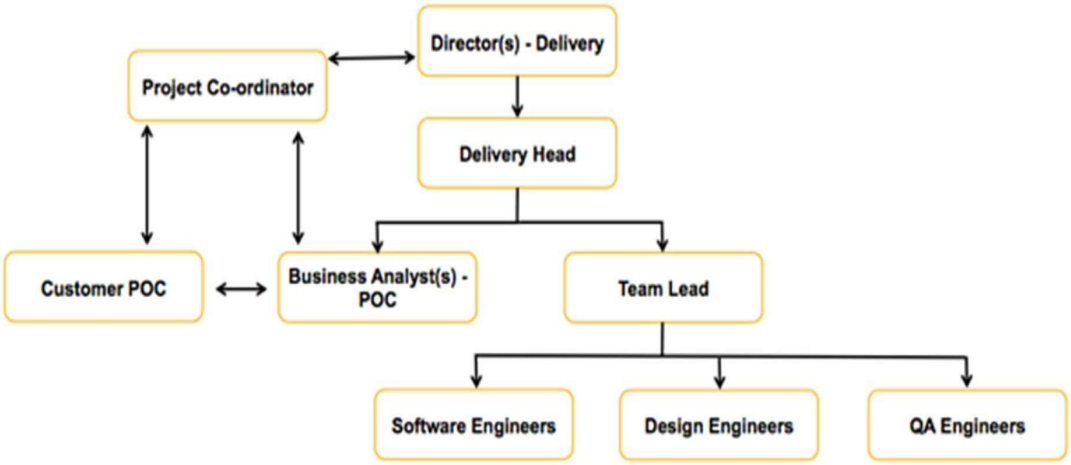

9 PROJECT ESTIMATION

Project Deployment Cost		
Sl. No.	**Deliverables**	**Cost (INR)**
1	Web Admin & Customer Portal with the above said features	INR 5,00,000
	Total Project Development Cost	**INR 5,00,000**
	GST (18%)	INR 90,000
	GRAND TOTAL	**INR 5,90,000/-**
3	Installation, Technical Support, Warranty, System Maintenance, Training (Online & Offline- Trivandrum) etc for a period of 6 months	FREE

Rupees Five lakh Ninety Thousand (Including all Taxes)

*The Price May vary if any change in the requirements or features mentioned in the section 6.

* Domain, Hosting Server, SSL, cPanel etc are not included.

*Implementation will be done online and Trainings can be done at Trivandrum (out of Trivandrum training cost will be extra).

*Onsite deployment (out of Trivandrum) will be extra if required

A) Delivery Timeline

Based on the requirements shared (Mentioned in Section 7), timeline to delivery the solution: within 45-60 business days from the date of acceptance of work order.

B) Customization Charges

Extra customizations apart from the requirements listed in this proposal shall charge on hourly basis (INR 1250 per Man hour).

C) Warranty

One year of free Warranty as per Kerala Startup Mission Policy

D) Change Requests

Change requests - hourly rate will be charged INR 1250 per Man hour).

E) AMC Charges

After the warranty period. *AMC – 10% of the total project cost

F) Hosting Spec & Cost

It is decided to go with Kerala State Data Centre, if so please ensure cPanel and SSL installation in it.

AWS Hosting cost will be extra which will be planned before the deployment (if required).

G) Payment Terms

- 10% Advance upon commencing the work.
- 50% upon submitting the Final designs of both User and Admin Interfaces.
- 25% upon hosting in the Staging server for Security Testing/Auditing
- 15% after Go-Live (Public Access)

10. RESPONSIBILITIES

- Provide dedicated Point of Contact for any project related queries
- Make timely decisions, if any, on issues escalated by IPROMISE team
- Ensure timely release of payment against the milestones cited above table.

11 PROJECT RELATED ASSUMPTIONS

- The project is subject to the respective government policies and regulations
- It is also assumed that any further changes to the scope will be done by mutual consent
- Any changes suggested by the client after freezing the specifications mentioned in the document will be estimated separately after doing an impact analysis and the additional cost will be added to the project cost
- Depending upon the effort required for changes the delivery schedule also may vary
- Any current issues are communicated by customer and shall be handled through the change request.
- Default language support is English
- Web application will be compatible in latest versions of Chrome and Firefox.

12 TIME LINE

- During the execution of this project, IPROMISE will provide multiple deliverables for review and acceptance.
- Any major change will have an impact on the deliverable and this may have a cascading effect on the other deliverables depending on its complexity.

Private & Confidential – Ipromise Solutions Pvt. Ltd.

IPROMISE SOLUTIONS

12 SUPPORT - SLA

PRIORITY LEVEL	DESCRIPTION	RESPONSE TIME (MINS)	RESTORATION TIME (WORKAROUND / SOLUTION)	SERVICE LEVEL TARGET
P1 - Critical Priority (Very high)	# An entire business critical system and/or service of system or part of system is unavailable, affecting more than 50% users (if not because of server issues)	15 – 30	Within 2 Hours in business hours & 6 to 12 hours for non business hours	99.90%
P2 - High Priority	# Business critical system and/or service is severely degraded affecting 25-50% users or partial loss of mission critical features/ functionality. # Non-business critical system and/ or service is unavailable, affecting more than 50% of users.	15 – 30	Within 4 Hours in business hours & within 24hours for non business hours	99.90%
P3 - Medium Priority	# Non - business critical system and/or services is severely degraded or having impact on 25-50% users # Business critical system and/or service is partially degraded affecting less than 25% users or non- business Critical functions or features are non-operational or unavailable to users	30 – 60	Within 2 - 3 days	99.90%
P4 - Low Priority	Incidents, which are not classified as P1/P2 or P3.	60 – 120	Within 4 - 5 days	99.90

Private & Confidential – Ipromise Solutions Pvt. Ltd.

13 CONTACT US

IPROMISE SOLUTIONS PVT. LTD.
2nd Floor, Penta City Tower,
Opp.PRS Hospital,Killipalam
Trivandrum, Kerala, IN
ceo@ipromisesolutions.com
www.ipromiseolutions.com

+91-9895373751, 0471-3570897

Copyright © 2023 IPROMISE
This document is confidential and should not be shared with any third party without the written authorization of IPROMISE. Any product/service names used in this document may be trademarks or service marks
